




Road Commission of Kalamazoo County
Weekly Project Updates

HAVE YOU SIGNED UP?

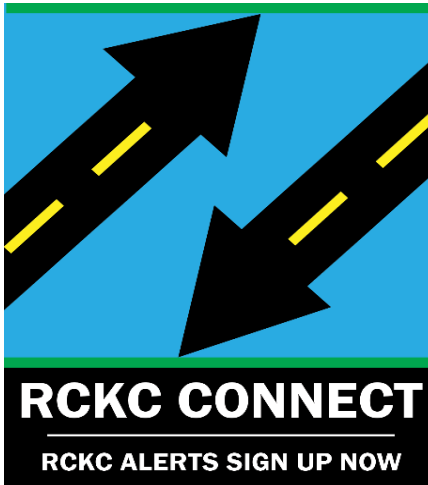

Sign up for RCKC CONNECT to receive message alerts for road construction, road closures/detours, and general public news from the Road Commission of Kalamazoo County website at: www.kalamazoocountyroads.com

Kalamazoo, MI-

In an effort to keep local drivers informed of the latest traffic and road maintenance operations by the Road Commission, we have provided the following update. For further information call 269-381-3170 or visit RCKC website www.kalamazoocountyroads.com.

“This information is made available to assist motorists in planning for construction delays,” Travis Bartholomew, Managing Director of the Road Commission said. “Motorists are reminded to **be alert, slow down, stay informed, and be cautious when approaching a the work zone** . Remember, these projects signify progress in improving our infrastructure!”

Please note: This information is subject to change. Projects, road closures and timing can change from day to day, depending upon a number of factors, and traffic delays can develop in a matter of minutes due to weather conditions, emergency situations, etc.

Charleston Township

Road: **38th Street - 4,672' south of G Avenue to 528' south of G Avenue**
Current Status: Week of 4/14 gravel will be placed on road surface in preparation for pulverizing
Detour: **None**
Project Information: Gravel / Pulverize / HMA Base Paving
Start Date: April 14, 2025
End Date: October 15, 2025

Comstock Township

Road: **Sprinkle Road - I-94 BL to 581' north of Lake Street**
Current Status: Median work should be wrapping up and the contractor will start on the east edge of Sprinkle Road the week of 4/14. The lane closure will change to be the outside northbound lane of Sprinkle Road for this work.
Detour: **Lane closures are anticipated. No closure and detour of the roadway is anticipated.**
Project Information: 1.0 miles of construction of concrete shoulder and median, rumble strips, and paving.
Start Date: April 7, 2025
End Date: June 14, 2025

Pavilion Township

Road: **Q Avenue - 29th Street to 34th Street**
Current Status: Tree removals and other clearing continuing into early April.
Detour: **Q Avenue will be closed to through traffic during the project. The detour route is 29th Street, S Avenue, and 36th Street.**
Project Information: This project includes tree clearing, crushing the existing asphalt to gravel sized pieces and mixed with the existing gravel, widening of shoulder, paving, and drainage improvements including some ditching.
Start Date: March 17, 2025
End Date: August 4, 2025

Richland Township

Road: **G Avenue - 28th Street to 38th Street (Richland / Ross Townships)**
Current Status: Traffic control signage anticipated to be setup on 4/14. The contractor is expected to start culvert work at G Avenue east of 32nd Street. A detour for G Avenue will be in effect.

Detour: **G Avenue will be closed to through traffic east of 32nd Street during phase 1 of the project. The detour route is 32nd Street, M-96, and 35th Street.**

Project Information: Center left turn lane construction at 5 intersections along G Avenue at 28th Street, 31st Street, 32nd Street, 35th Street, and 38th Street. Project includes road widening for turn lanes, paving, and drainage improvements including some ditching.

Start Date: April 11, 2025

End Date: August 31, 2025

###
