




**Road Commission of Kalamazoo County
Weekly Project Updates**

HAVE YOU SIGNED UP?

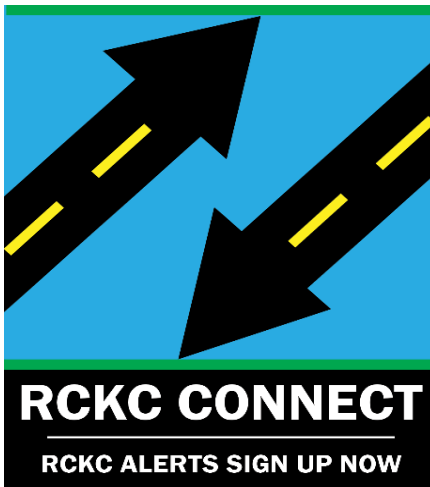

Sign up for RCKC CONNECT to receive message alerts for road construction, road closures/detours, and general public news from the Road Commission of Kalamazoo County website at: www.kalamazoocountyroads.com

Kalamazoo, MI-

In an effort to keep local drivers informed of the latest traffic and road maintenance operations by the Road Commission, we have provided the following update. For further information call 269-381-3170 or visit RCKC website www.kalamazoocountyroads.com.

"This information is made available to assist motorists in planning for construction delays," Travis Bartholomew, Managing Director of the Road Commission said. "Motorists are reminded to ***be alert, slow down, stay informed, and be cautious when approaching a the work zone*** . Remember, these projects signify progress in improving our infrastructure!"

Please note: This information is subject to change. Projects, road closures and timing can change from day to day, depending upon a number of factors, and traffic delays can develop in a matter of minutes due to weather conditions, emergency situations, etc.

Alamo Township

Road: E Avenue – 1,270' east of Ravine Road to 2,850' east of Ravine Road
Current Status: Week of 5/19 Fine grading and drainage improvements
Detour: None
Project Information: Pulverize, Double Chip Seal
Start Date: April 21, 2025
End Date: October 15, 2025

Road: F Avenue – Ravine Road to 12th Street;
Current Status: Week of 5/19 roadside restoration
Detour: None
Project Information: HMA Overlay
Start Date: April 21, 2025
End Date: October 15, 2025

Road: 8th Street - G Avenue to Hart Drive
Current Status: Week of 5/19 Tree removal work will continue
Detour: Road Closed to Thru Traffic
Project Information: Gravel Pulverize, HMA Overlay, Drainage Improvements
Start Date: April 21, 2025
End Date: October 15, 2025

Brady Township

Road: 31st Street over Brown Creek
Current Status: Project projected to start 6/2. Road milling and tree and brush clearing to begin.
Detour: 31st Street will be closed to through traffic and detoured using YZ Avenue, 27th Street, Y Avenue, 24th Street, and W Avenue.
Project Information: Preventative maintenance work on this bridge including railing , guardrail, paving, and structural repairs.
Start Date: June 2, 2025
End Date: August 5, 2025

Road: Y Avenue over Portage Creek
Current Status: Project projected to start 6/2. Road milling and tree and brush clearing to begin.
Detour: Y Avenue will be closed to through traffic and detoured using 27th Street, YZ Avenue, 32nd Street, X Avenue, 31st Street, W Avenue, and 24th Street
Project Information: Preventative maintenance work on this bridge including railing , guardrail, paving, and structural repairs.
Start Date: June 2, 2025
End Date: July 3, 2025

Road: YZ Avenue over Brown Creek
Current Status: Project projected to start 6/2. Road milling and tree and brush clearing to begin.
Detour: YZ Avenue will be closed to through traffic and detoured using 32nd Street, X Avenue, 31st Street, W Avenue, and 24th Street, Y Avenue, and 27th Street
Project Information: Preventative maintenance work on this bridge including railing , guardrail, paving, and structural repairs.
Start Date: June 2, 2025
End Date: August 30, 2025

Charleston Township

Road: 38th Street - 4,672' south of G Avenue to 528' south of G Avenue
Current Status: Week of 5/19 Tree removal will continue, drainage updates and embankment work
Detour: Road Closed to Thru Traffic
Project Information: Gravel, Pulverize, HMA Base Paving
Start Date: April 14, 2025
End Date: October 15, 2025

Comstock Township

Road: Fawn Meadow Trail – 30th Street to 750' east of Antler Street, Spike Street – 225' south of Fawn Meadow Trail to Fawn Meadow Trail, Antler Street – Fawn Meadow Trail to Buck Avenue, Doe Avenue – Antler Street to 600' east of Antler Street, Roush Street – 200' south of Buck Avenue to Buck Avenue, Buck Avenue – 30th Street to 66'; east of Antler Street

Current Status: Awaiting Fog Seal construction joint
Detour: None
Project Information: Milling and Paving new HMA surface, drainage improvements
Start Date: April 23, 2025
End Date: October 15, 2025

Road: Sprinkle Road - I-94 BL to 581' north of Lake Street
Current Status: Concrete work anticipated for the week of 5/19 on the southbound lanes and west side of the roadway.
Detour: Lane closures are anticipated. No closure and detour of the roadway is anticipated.
Project Information: 1.0 miles of construction of concrete shoulder and median, rumble strips, and paving.
Start Date: April 7, 2025
End Date: June 14, 2025

Kalamazoo Township

Road: **Fairfield Avenue – West Main Street to 225’ north of Hilltop Street, Castle Street – Brook Drive to Fairfield Avenue, Seamers Street – Brook Drive to Fairfield Avenue, Hilltop Street – Brook Drive to Fairfield Avenue**

Current Status: Week of 5/19 manhole adjustments and fog seal construction joints to follow

Detour: **None**

Project Information: Milling, paving new surface, manhole adjustments and shoulder gravel

Start Date: April 23, 2025

End Date: October 15, 2025

Road: **Woodrow Drive – Texel Drive to Ashbury Avenue**

Current Status: Week of 5/19 manhole adjustments and fog seal construction joints to follow

Detour: **None**

Project Information: Milling, paving new surface, and shoulder gravel

Start Date: April 23, 2025

End Date: October 15, 2025

Road: **Seville Avenue – Shasta Drive to Monterey Drive, Oxford Street – 159’ south of Barclay Drive to Barclay Drive, Shasta Drive – Barclay Drive to Mosel Avenue, Monterey Drive – Shasta Drive to Seville Avenue, Monterey Circle – Monterey Drive to 142’ north of Monterey Drive**

Current Status: Week of 5/19 manhole adjustments and fog seal construction joints to follow

Detour: **None**

Project Information: Milling, paving new surface, manhole adjustments and shoulder gravel

Start Date: April 24, 2025

End Date: October 15, 2025

Road: **Avondale Drive – Craft Avenue to Craft Avenue, Avondale Circle – Avondale Circle to 130’ east of Avondale Drive**

Current Status: Week of 5/19 manhole adjustments and fog seal construction joints to follow

Detour: **None**

Project Information: Milling, paving new surface, manhole adjustments and shoulder gravel

Start Date: April 24, 2025

End Date: October 15, 2025

Road: Craft Avenue – Kenilworth Avenue to East Main Street
Current Status: Week of 5/19 manhole adjustments and fog seal construction joints to follow
Detour: None
Project Information: Milling, paving new surface, manhole adjustments and shoulder gravel

Start Date: May 1, 2025
End Date: October 15, 2025

Road: Chrysler Street – Kenilworth Avenue to East Main Street
Current Status: Week of 5/19 manhole adjustments and fog seal construction joints to follow
Detour: None
Project Information: Milling, paving new surface, manhole adjustments and shoulder gravel

Start Date: April 24, 2025
End Date: October 15, 2025

Road: Nelson Avenue – 954’ south of West Main Street to West Main Street

Current Status: Week of 5/19 manhole adjustments and fog seal construction joints to follow
Detour: None
Project Information: Milling, paving new surface, manhole adjustments and shoulder gravel

Start Date: April 24, 2025
End Date: October 15, 2025

Road: Gilkison Avenue – 954’ south of West Main Street to West Main Street

Current Status: Week of 5/19 manhole adjustments and fog seal construction joints to follow
Detour: None
Project Information: Milling, paving new surface, manhole adjustments and shoulder gravel

Start Date: April 24, 2025
End Date: October 15, 2025

Oshtemo Township

Road: 5th Street – 2,230' south of Stadium Drive to Stadium Drive, Gibbs Street – 5th Street to O'Park Street, O'Park Street – 2,020' south of Stadium Drive to Stadium Drive, Frie Avenue – O'Park Street to 6th Street

Current Status: Fog Seal construction joint to follow

Detour: None

Project Information: Milling, new HMA surface and shoulder gravel

Start Date: April 28, 2025

End Date: October 15, 2025

Pavilion Township

Road: Q Avenue - 29th Street to 34th Street

Current Status: Clearing, installing SESC measures, and lowering monuments week of 5/19.

Detour: Q Avenue will be closed to through traffic during the project. The detour route is 29th Street, S Avenue, and 36th Street.

Project Information: This project includes tree clearing, crushing the existing asphalt to gravel sized pieces and mixed with the existing gravel, widening of shoulder, paving, and drainage improvements including some ditching.

Start Date: March 17, 2025

End Date: August 4, 2025

Richland Township

Road: G Avenue - 28th Street to 38th Street (Richland / Ross Townships)

Current Status: Paving is anticipated at the intersection of G Avenue at 28th Street Early during the week of 5/19. Road widening on the north side of the intersections at 31st Street, 32nd Street, 35th Street, and 38th Street. Traffic will be maintained at these intersections during work.

Detour: G Avenue will be closed to through traffic at 28th Street. The detour route is 32nd Street and Gull Road. 28th Street will also be closed to through traffic. The detour route is Gull Road, Sprinkle Road, and H Avenue.

Project Information: Center left turn lane construction at 5 intersections along G Avenue at 28th Street, 31st Street, 32nd Street, 35th Street, and 38th Street. Project includes road widening for turn lanes, paving, and drainage improvements including some ditching.

Start Date: April 11, 2025

End Date: August 31, 2025

Schoolcraft Township

Road: Hopewell Street - South Hill Avenue to Crimora Street
Current Status: Fog Seal construction joint to follow
Detour: None
Project Information: Milling and paving new HMA surface
Start Date: April 24, 2025
End Date: October 15, 2025

Road: Shaver Road - US 131 to 6,864' north of US 131
Current Status: Milling and paving week of 5/19
Detour: None
Project Information: This project includes drainage improvements, paving, and restoration.

Start Date: May 7, 2025
End Date: July 2, 2025

Texas Township

Road: Torrey Pines Drive – Cypress Bay Drive to Veronica Street, Stapleton Drive – Torrey Pines Drive to 12th Street, Stoneybrook Road – Burning Tree Road (west) to 12th Street, Hunters Ridge Drive – Heathrow Avenue to Cypress Bay Drive, Snowbird Court – Hunters Ridge Drive to Hunters Ridge Drive; Telluride Drive - 1,088' west of Hunters Ridge Drive to Hunters Ridge Drive
Current Status: Week of 5/19 manhole adjustments and surface paving
Detour: None
Project Information: Milling and paving new HMA surface
Start Date: May 12, 2025
End Date: October 15, 2025

Road: Veronica Street – Cypress Bay Drive to Queen Victoria Lane, Lewsinda Avenue (west) – 213' west of Marsha Street to Veronica Street; Marsha Street – Lewsinda Avenue to 135' north of Lewsinda Avenue, Lewsinda Avenue (east) – Veronica Street to 12th Street, Anthony Street – Lewsinda Avenue to 121' north of Lewsinda Avenue

Current Status: Week of 5-19 manhole adjustments, milling and surface paving
Detour: None
Project Information: Milling and paving new HMA surface
Start Date: May 15, 2025
End Date: October 15, 2025

County Wide Projects

Road: Crack Filling on various roads in Kalamazoo County
Current Status: Various Locations
Detour: None
Project Information: Various County-wide
Start Date: May 12, 2025
End Date: October 15, 2025

###
