




Road Commission of Kalamazoo County  
Weekly Project Updates

HAVE YOU SIGNED UP?

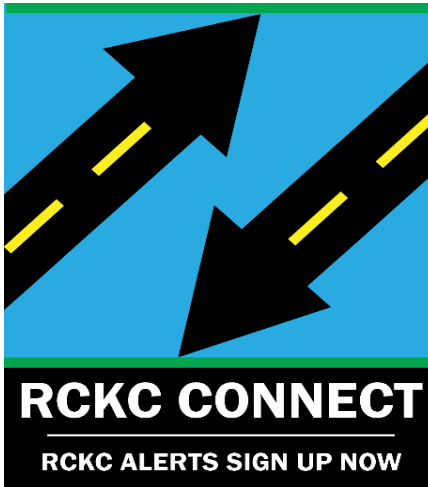

Sign up for RCKC CONNECT to receive message alerts for road construction, road closures/detours, and general public news from the Road Commission of Kalamazoo County website at: [www.kalamazoocountyroads.com](http://www.kalamazoocountyroads.com)

Kalamazoo, MI-

In an effort to keep local drivers informed of the latest traffic and road maintenance operations by the Road Commission, we have provided the following update. For further information call 269-381-3170 or visit RCKC website [www.kalamazoocountyroads.com](http://www.kalamazoocountyroads.com).

“This information is made available to assist motorists in planning for construction delays,” Travis Bartholomew, Managing Director of the Road Commission said. “Motorists are reminded to **be alert, slow down, stay informed, and be cautious when approaching a the work zone** . Remember, these projects signify progress in improving our infrastructure!”

*Please note: This information is subject to change. Projects, road closures and timing can change from day to day, depending upon a number of factors, and traffic delays can develop in a matter of minutes due to weather conditions, emergency situations, etc.*

**Alamo Township**

**Road:** E Avenue – 1,270’ east of Ravine Road to 2,850’ east of Ravine Road  
**Current Status:** Week of 5/26 Fine grading and drainage improvements  
**Detour:** None  
**Project Information:** Pulverize, Double Chip Seal  
**Start Date:** April 21, 2025  
**End Date:** October 15, 2025

**Road:** F Avenue – Ravine Road to 12th Street;  
**Current Status:** Week of 5/26 fog seal construction joint  
**Detour:** None  
**Project Information:** HMA Overlay  
**Start Date:** April 21, 2025  
**End Date:** October 15, 2025

**Road:** 8th Street - G Avenue to Hart Drive  
**Current Status:** Week of 5/26 Tree removal work will continue  
**Detour:** Road Closed to Thru Traffic  
**Project Information:** Gravel Pulverize, HMA Overlay, Drainage Improvements  
**Start Date:** April 21, 2025  
**End Date:** October 15, 2025

\*\*\*\*\*

**Brady Township**

**Road:** 31st Street over Brown Creek  
**Current Status:** Project projected to start 6/2. Road milling and tree and brush clearing to begin.  
**Detour:** 31st Street will be closed to through traffic and detoured using YZ Avenue, 27th Street, Y Avenue, 24th Street, and W Avenue.  
**Project Information:** Preventative maintenance work on this bridge including railing , guardrail, paving, and structural repairs.  
**Start Date:** June 2, 2025  
**End Date:** August 5, 2025

**Road:** Y Avenue over Portage Creek  
**Current Status:** Project projected to start 6/2. Road milling and tree and brush clearing to begin.  
**Detour:** Y Avenue will be closed to through traffic and detoured using 27th Street, YZ Avenue, 32nd Street, X Avenue, 31st Street, W Avenue, and 24th Street  
**Project Information:** Preventative maintenance work on this bridge including railing , guardrail, paving, and structural repairs.  
**Start Date:** June 2, 2025  
**End Date:** July 3, 2025

**Road:** YZ Avenue over Brown Creek  
**Current Status:** Project projected to start 6/2. Road milling and tree and brush clearing to begin.  
**Detour:** YZ Avenue will be closed to through traffic and detoured using 32nd Street, X Avenue, 31st Street, W Avenue, and 24th Street, Y Avenue, and 27th Street  
**Project Information:** Preventative maintenance work on this bridge including railing , guardrail, paving, and structural repairs.  
**Start Date:** June 2, 2025  
**End Date:** August 30, 2025

\*\*\*\*\*

**Charleston Township**

**Road:** 38th Street - 4,672' south of G Avenue to 528' south of G Avenue  
**Current Status:** Week of 5/26 Tree removal will continue, drainage updates and embankment work  
**Detour:** Road Closed to Thru Traffic  
**Project Information:** Gravel, Pulverize, HMA Base Paving  
**Start Date:** April 14, 2025  
**End Date:** October 15, 2025

\*\*\*\*\*

**Comstock Township**

**Road:** Fawn Meadow Trail – 30th Street to 750' east of Antler Street, Spike Street – 225' south of Fawn Meadow Trail to Fawn Meadow Trail, Antler Street – Fawn Meadow Trail to Buck Avenue, Doe Avenue – Antler Street to 600' east of Antler Street, Roush Street – 200' south of Buck Avenue to Buck Avenue, Buck Avenue – 30th Street to 66'; east of Antler Street  
**Current Status:** Awaiting Fog Seal construction joint  
**Detour:** None  
**Project Information:** Milling and Paving new HMA surface, drainage improvements  
**Start Date:** April 23, 2025  
**End Date:** October 15, 2025

**Road:** Sprinkle Road - I-94 BL to 581' north of Lake Street  
**Current Status:** Paving anticipated for the week of 5/26 on the northbound lanes and east side of the roadway.  
**Detour:** Lane closures are anticipated. No closure and detour of the roadway is anticipated.  
**Project Information:** 1.0 miles of construction of concrete shoulder and median, rumble strips, and paving.  
**Start Date:** April 7, 2025  
**End Date:** June 14, 2025

\*\*\*\*\*

Kalamazoo Township

**Road:** **Fairfield Avenue – West Main Street to 225’ north of Hilltop Street, Castle Street – Brook Drive to Fairfield Avenue, Seamers Street – Brook Drive to Fairfield Avenue, Hilltop Street – Brook Drive to Fairfield Avenue**

**Current Status:** Week of 5/26 fog seal construction joints  
**Detour:** **None**  
**Project Information:** Milling, paving new surface, manhole adjustments and shoulder gravel  
**Start Date:** April 23, 2025  
**End Date:** October 15, 2025

**Road:** **Woodrow Drive – Texel Drive to Ashbury Avenue**  
**Current Status:** Week of 5/26 manhole adjustments and fog seal construction joints to follow  
**Detour:** **None**  
**Project Information:** Milling, paving new surface, and shoulder gravel  
**Start Date:** April 23, 2025  
**End Date:** October 15, 2025

**Road:** **Seville Avenue – Shasta Drive to Monterey Drive, Oxford Street – 159’ south of Barclay Drive to Barclay Drive, Shasta Drive – Barclay Drive to Mosel Avenue, Monterey Drive – Shasta Drive to Seville Avenue, Monterey Circle – Monterey Drive to 142’ north of Monterey Drive**  
**Current Status:** Week of 5/26 manhole adjustments and fog seal construction joints to follow  
**Detour:** **None**  
**Project Information:** Milling, paving new surface, manhole adjustments and shoulder gravel  
**Start Date:** April 24, 2025  
**End Date:** October 15, 2025

**Road:** **Avondale Drive – Craft Avenue to Craft Avenue, Avondale Circle – Avondale Circle to 130’ east of Avondale Drive**  
**Current Status:** Week of 5/26 manhole adjustments and fog seal construction joints to follow  
**Detour:** **None**  
**Project Information:** Milling, paving new surface, manhole adjustments and shoulder gravel  
**Start Date:** April 24, 2025  
**End Date:** October 15, 2025

**Road:** **Craft Avenue – Kenilworth Avenue to East Main Street**  
Current Status: Week of 5/26 manhole adjustments and fog seal construction joints to follow  
**Detour:** **None**  
Project Information: Milling, paving new surface, manhole adjustments and shoulder gravel  
Start Date: May 1, 2025  
End Date: October 15, 2025

**Road:** **Chrysler Street – Kenilworth Avenue to East Main Street**  
Current Status: Week of 5/26 manhole adjustments and fog seal construction joints to follow  
**Detour:** **None**  
Project Information: Milling, paving new surface, manhole adjustments and shoulder gravel  
Start Date: April 24, 2025  
End Date: October 15, 2025

**Road:** **Nelson Avenue – 954' south of West Main Street to West Main Street**  
Current Status: Week of 5/26 manhole adjustments and fog seal construction joints to follow  
**Detour:** **None**  
Project Information: Milling, paving new surface, manhole adjustments and shoulder gravel  
Start Date: April 24, 2025  
End Date: October 15, 2025

**Road:** **Gilkison Avenue – 954' south of West Main Street to West Main Street**  
Current Status: Week of 5/26 manhole adjustments and fog seal construction joints to follow  
**Detour:** **None**  
Project Information: Milling, paving new surface, manhole adjustments and shoulder gravel  
Start Date: April 24, 2025  
End Date: October 15, 2025

\*\*\*\*\*

**Oshtemo Township**

**Road:** 5th Street – 2,230’ south of Stadium Drive to Stadium Drive, Gibbs Street – 5th Street to O’Park Street, O’Park Street – 2,020’ south of Stadium Drive to Stadium Drive, Frie Avenue – O’Park Street to 6th Street

Current Status: Fog Seal construction joint to follow

**Detour:** None

Project Information: Milling, new HMA surface and shoulder gravel

Start Date: April 28, 2025

End Date: October 15, 2025

\*\*\*\*\*

**Pavilion Township**

**Road:** T Avenue – 3,500’ east of 34th Street to 4,500’ east of 34th Street

Current Status: Wedging complete, gravel shoulders to follow

**Detour:** None

Project Information: HMA wedging

Start Date: April 24, 2025

End Date: October 15, 2025

**Road:** Q Avenue - 29th Street to 34th Street

Current Status: Clearing, installing SESC measures, and lowering monuments week of 5/26.

**Detour:** Q Avenue will be closed to through traffic during the project. The detour route is 29th Street, S Avenue, and 36th Street.

Project Information: This project includes tree clearing, crushing the existing asphalt to gravel sized pieces and mixed with the existing gravel, widening of shoulder, paving, and drainage improvements including some ditching.

Start Date: March 17, 2025

End Date: August 4, 2025

\*\*\*\*\*

**Richland Township**

**Road:** **G Avenue - 28th Street to 38th Street (Richland / Ross Townships)**  
**Current Status:** Road widening on the north side of the intersections at 31st Street, 32nd Street, 35th Street, and 38th Street. Traffic will be maintained at these intersections during work.  
**Detour:** **G Avenue will be closed to through traffic at 28th Street. The detour route is 32nd Street and Gull Road. 28th Street will also be closed to through traffic. The detour route is Gull Road, Sprinkle Road, and H Avenue.**

**Project Information:** Center left turn lane construction at 5 intersections along G Avenue at 28th Street, 31st Street, 32nd Street, 35th Street, and 38th Street. Project includes road widening for turn lanes, paving, and drainage improvements including some ditching.

**Start Date:** April 11, 2025  
**End Date:** August 31, 2025

\*\*\*\*\*

**Schoolcraft Township**

**Road:** **Hopewell Street - South Hill Avenue to Crimora Street**  
**Current Status:** Fog Seal construction joint to follow  
**Detour:** **None**  
**Project Information:** Milling and paving new HMA surface  
**Start Date:** April 24, 2025  
**End Date:** October 15, 2025

**Road:** **Shaver Road - US 131 to 6,864' north of US 131**  
**Current Status:** Milling, paving, & placing shoulder gravel week of 5/26  
**Detour:** **None**  
**Project Information:** This project includes drainage improvements, paving, and restoration.

**Start Date:** May 7, 2025  
**End Date:** July 2, 2025

**Road:** U Avenue / 23rd Street - 22nd Street to 375' south of TU Avenue  
**Current Status:** Driveway adjustments and installing culverts week of 5/26  
**Detour:** U Avenue will be closed to through traffic from 22nd Street to 23rd Street. 23rd Street will also be closed to through traffic from U Ave to TU Ave. The detour route is Sprinkle Road, V Avenue, N Richardson Street, E Prairie Street, S Main Street, W Avenue, and Portage Road.

**Project Information:** This project includes crushing the existing asphalt to gravel sized pieces and mixing with the existing gravel, widening of shoulder, paving, and drainage improvements with some ditching.

**Start Date:** May 28, 2025  
**End Date:** August 15, 2025

\*\*\*\*\*

**Texas Township**

**Road:** Torrey Pines Drive – Cypress Bay Drive to Veronica Street, Stapleton Drive – Torrey Pines Drive to 12th Street, Stoneybrook Road – Burning Tree Road (west) to 12th Street, Hunters Ridge Drive – Heathrow Avenue to Cypress Bay Drive, Snowbird Court – Hunters Ridge Drive to Hunters Ridge Drive; Telluride Drive - 1,088' west of Hunters Ridge Drive to Hunters Ridge Drive

**Current Status:** Week of 5/26 manhole adjustments and surface paving

**Detour:** None

**Project Information:** Milling and paving new HMA surface

**Start Date:** May 12, 2025  
**End Date:** October 15, 2025

**Road:** Veronica Street – Cypress Bay Drive to Queen Victoria Lane, Lewsinda Avenue (west) – 213' west of Marsha Street to Veronica Street; Marsha Street – Lewsinda Avenue to 135' north of Lewsinda Avenue, Lewsinda Avenue (east) – Veronica Street to 12th Street, Anthony Street – Lewsinda Avenue to 121' north of Lewsinda Avenue

**Current Status:** Week of 5/26 manhole adjustments, milling and surface paving

**Detour:** None

**Project Information:** Milling and paving new HMA surface

**Start Date:** May 15, 2025  
**End Date:** October 15, 2025

\*\*\*\*\*

**County Wide Projects**

**Road:** Crack Filling on various roads in Kalamazoo County

**Current Status:** Various Locations

**Detour:** None

**Project Information:** Various County-wide

**Start Date:** May 12, 2025  
**End Date:** October 15, 2025
